



14<sup>th</sup> Street Streetscape Project N.W. From  
Thomas Circle to Florida Ave  
DC Contract No.: DCKA-2016-C-0043

FAP No.: STP-2016 (054)

---

**CONSTRUCTION MANAGER'S  
WEEKLY PROGRESS REPORT**

04/19/2020 - 04/25/2020

---

**Project Website:** [www.14thstreetproject.com](http://www.14thstreetproject.com)



FMCC Restoring damaged Signal foundation at Q street

**PREPARED BY**      **Kendry A. Contreras**

A handwritten signature in blue ink, appearing to read 'Kendry A. Contreras'.

## 1. EXECUTIVE SUMMARY

### Project Description:

The scope of the construction work includes the followings:

- The removal and disposal of existing roadway pavement, curb and gutter and sidewalks, milling of existing asphalt pavement to the extents shown on plans.
- The resurfacing of existing asphalt pavement using 2" Superpave AC surface on 14<sup>th</sup> Street between Thomas Circle and Florida Ave as shown in the plans.
- The replacement of all curbs and gutters with Granite Curbs, 12" Brick Gutter, Concrete Sidewalk, Wheelchair/Bicycle Ramps, and Cobble Stone LID Paver, Bioretention Planters as shown on the plans or as directed.
- The removal and transportation to storage yard of Existing Traffic Signals and Light Poles as shown on plans. Traffic signal relocation and equipment upgrading of Traffic Signals at all intersections of 14<sup>th</sup> Street within the project limit as shown on plans.
- Streetscaping throughout the 14<sup>th</sup> Street corridor as shown in the plans.
- The installation of traffic signing and permanent pavement markings.
- Upgrading of street lighting throughout the 14<sup>th</sup> Street corridor as shown in the plans.
- Construction and upgrading of single catch basin, double catch basin, and triple catch basin.
- Construction / Upgrading of new Watermains, Fire Hydrants
- Full Reconstruction of R Street.
- Installation of new Bus Islands and bus pads as shown on the plans and as directed.
- The installation and use of erosion and sediment control measures as required.
- Mobilization and demobilization, performance of field layout, provision and maintenance of engineer's field facilities, progress photographs, and the proper maintenance of vehicular and pedestrian traffic during construction, including provision of all required construction warning and detour signs and traffic control devices.

## 2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

### Progress Summary:

1. Electricians completed light pole splicing, Began removing cabinets and 5 left over T bases
2. Omni continue parking and cleaning their inlets
3. Striping Crosswalks and Permanent Parking lanes/ Bike lanes. Layout, north of V
4. Damaged Q street signal pole foundations demo, formed and re poured
5. FMCC worked on punchlist items
6. Inlaid Pavement marking Installed at W and V streets
7. Restore section of sidewalk that were removed
8. D.E.N. working on punchlist work

### PM Community Outreach Activities:

9. TBA personnel continues to respond to questions that come through project portal.
10. Reply to public concerns regarding the Corona virus

3. QC/ ISSUES / ACTION ITEMS

- Permanent high contrast tape is in back order. DCline just recently ordered, and probably will not be available for some months. Only major risk for the project
- Final Punchlist for D.E.N. issued on 04/06.They began working on it all week.
- TC and TEC cabinets can be removed now per Harvey
- Omni working on punch list of their structures. DCwater signed off on the bulk of catch inlets, still need to clean more
- FMCC needs additional resources to complete the punch lists and all work related to the project by the April 30<sup>th</sup> deadline

**ACTION ITEMS. -**

Action	Description	Action By	Original Date	Expected Date	Status
001	Address the MOT, safety issues within the corridor.	FMCC/Kevin Felix	June 5, 2019	April 28, 2020	Ongoing
002	Coordinate Mr. Jermaine Quattlebaum complete the punch list for DC Water work.	Omni/Mr. Juan Vega	August 06, 2019	April 28, 2020	Ongoing
003	Showing DDOT the price difference of the luminaire with and without the glare shield.	FMCC Electrical	January 21, 2020	April 28, 2020	Ongoing
004	Submit the price proposal for reinstall of the blue historical signs	FMCC/Abdalla Elsheikh	January 21, 2020	April 28, 2020	Ongoing
005	Confirm with DC Water that the watermain tie-in location is ready for work on 04/15/2020	CM Team	April 14, 2020	April 14, 2020	New

4. MEETINGS/ PROJECT COORDINATION

- New Progress Meeting are schedule via teleconference every other Tuesday at 10:30am.

5. DAILY WORK PERFORMED

**Monday 04/20/2020**

**FMCC** was onsite providing MOT devices for work including:

- Striping operations intersection of 14<sup>th</sup> Street and T street.
- Removing Q street foundation (damaged NW corner pole)

**FMCC Electrical crew** was onsite at the corner of Q street relocating the damaged pole onto a temporary foundation

**FMCC Civil Crew** was on site demoing the damage foundation on the NWC of Q street . They remove top of portion, Clean around conduit and anchor bolts. Form the new foundation to be ready to pour.

**Omni** was working today cleaning and fixing catch basin at various locations  
**DC-Line** .- Was today onsite striping crosswalk and intersection 14<sup>th</sup> Street and T street.

## **Tuesday 04/21/2020**

**FMCC** was onsite providing MOT devices for work including:

- Relocation of the foundation at NWC of Q Street
- Removal of the T-base at NEC of Q Street
- DC -Line striping work along the corridor
- DEN punch list work items.

**FMCC Electrical crew** was onsite relocating the foundation at NWC of Q Street and removing the T-base at NEC of Q Street.

**DC-Line** worked on striping work.

**Omni** was not onsite today.

**DEN** has crew working on addressing punch list items.

## **Wednesday 04/22/2020**

**FMCC Civil** removed 5 T-bases and restore the sidewalk (3 at Q street, 1 at R street and 1 at W street)

**DC line** was today onsite striping crosswalk and intersection 14<sup>th</sup> Street and T street.

**FMCC** was notified via email of the several deficiencies along the corridor and the one week timeframe to get them taken care. No other work was seen happening.

## **Thursday, 04/23/2020**

**FMCC** was onsite providing MOT devices for work including:

- Inlet raising at SWC of S Street
- Trash can removal along the corridor
- DC-Line striping work near V Street northbound
- Thermoplastic Inlaid Pavement system at T Street and W Street

**FMCC** was on site raising the inlet at SWC of S Street and remove some trash cans along the corridor

**DC-Line** worked on striping work near V Street northbound

Inlaid Thermoplastic Pavement Marking System was installed at West side of T Street and W Street

**FMCC** has crew working on addressing punch list items.

## Friday, 04/24/2020

At 7:40 AM. CM Kendry Contreras was notified via email by Mr Constantino that due to severe weather contractor was cancelling all activities.

At 7:50 AM. Mr. Ramesh Mirchandani called CM and officially shutdown the project. No other work was performed

## Saturday, 04/25/2020

**FMCC** provided MOT Devices.

**FMCC Civil** patched sidewalks in various places on 14<sup>th</sup> street corridor which are part of the original punch list items, installed trash can in front of the brick church

**FMCC Electrical** removed 4 Traffic Cabinets, streetlight poles

**DC Line** worked on Lane markings at Intersection of 14th and Florida avenue

## 7. RFI's/SUBMITTALS

### 1. Requests for Information:

- To date, we have received **51** RFIs; **50** RFIs have been answered.
- Glare shield RFI submitted to streetlight division. Received invoices in current review

### 2. Submittals:

- We have received **87** Submittals; **87** Submittals have been Approved.

## 8. CHANGE ORDERS/TASK ORDERS

- Price breakdown for add water work received from FMCC. Tie-in were priced separately. Pepco sent letter on 12/14 accepting and taking responsibility of the CO. Sent Article 3 letter to FMCC on 12.20. Received commitment from DCwater to write Change. Quantity for Tie-in was estimated. With Final Qtys. FMCC has revised Change order, waiting for their signature
- Extended OH cost. Waiting for FMCC to provide justification and breakdown
- Work with DDOT in providing MOD 5 to ATCS to cover part time in June cost for CM and OE

## 9. DBE or CBE PARTICIPATION SUMMARIES

### 3. ATCS CBE / DBE Activity:

- Hayat Brown LLC.: Provided Office Engineering and Inspection support for this project.
- Cube root: Provided Inspection support
- Tina Boyd- PR and Outreach support, webpage management

### 4. Fort Myer Construction Corp. DBE Activity:

- Omni Excavators Inc.
- Den United LLC.
- DC Line
- Cooper landscaping
- Long Fence
- Capital Flexible pavement
- Driveway impressions

## 10. ACCIDENTS/INCIDENT

## 11. PHOTOS OF WORK PERFORMED THIS PERIOD



DC Line removing old lane marking




FMCC patching sidewalks at s/w/c of U & 14<sup>th</sup> street



Inlet was delivered to the SWC of S Street



FMCC was on site for some punchlist work items

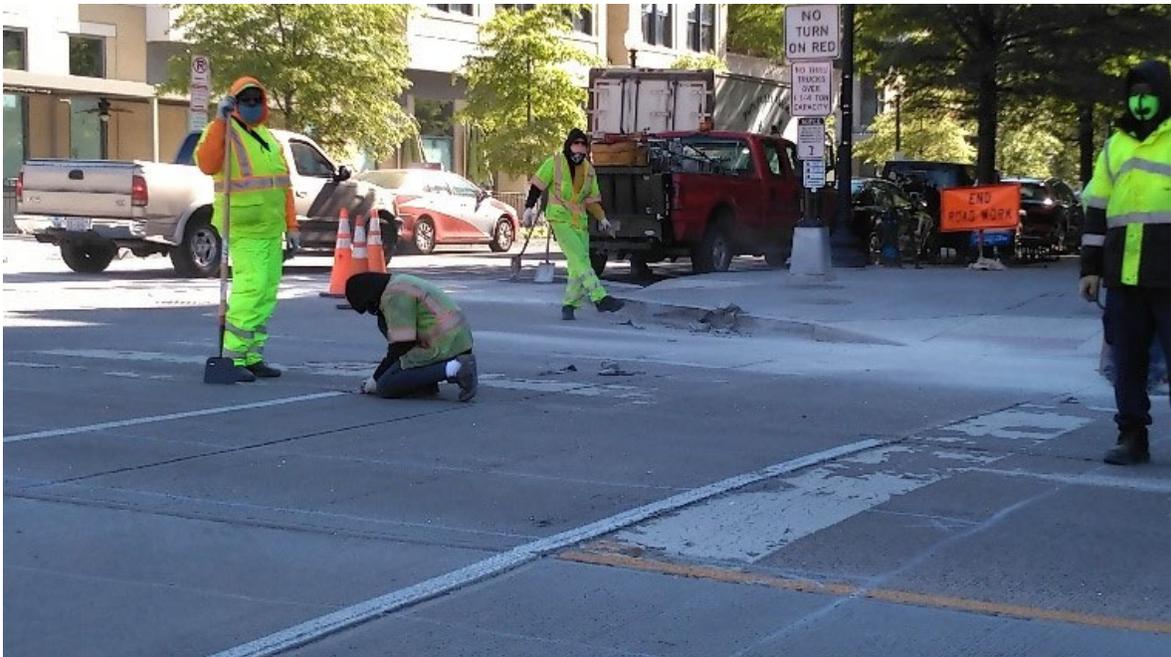

DCLine removing temporary tape at W street



FMCC restoring sidewalk after T-base removal



FMCC working on removing the T-base at NEC of Q Street



DEN was on site working on punch list items



Demo and removal of cracked foundation Q Street



Layout Q street Striping
